



PROJECT UPDATE  
NOVEMBER 2021

## PROJECT INFORMATION



Project: **ALogis Naic 2**

Location: **Cavite Technopark, Barangay Sabang Naic, Cavite**

Total Land Area: **26,876 square meters**


Total GLA: **15,576 square meters**

No. of Units: **13**

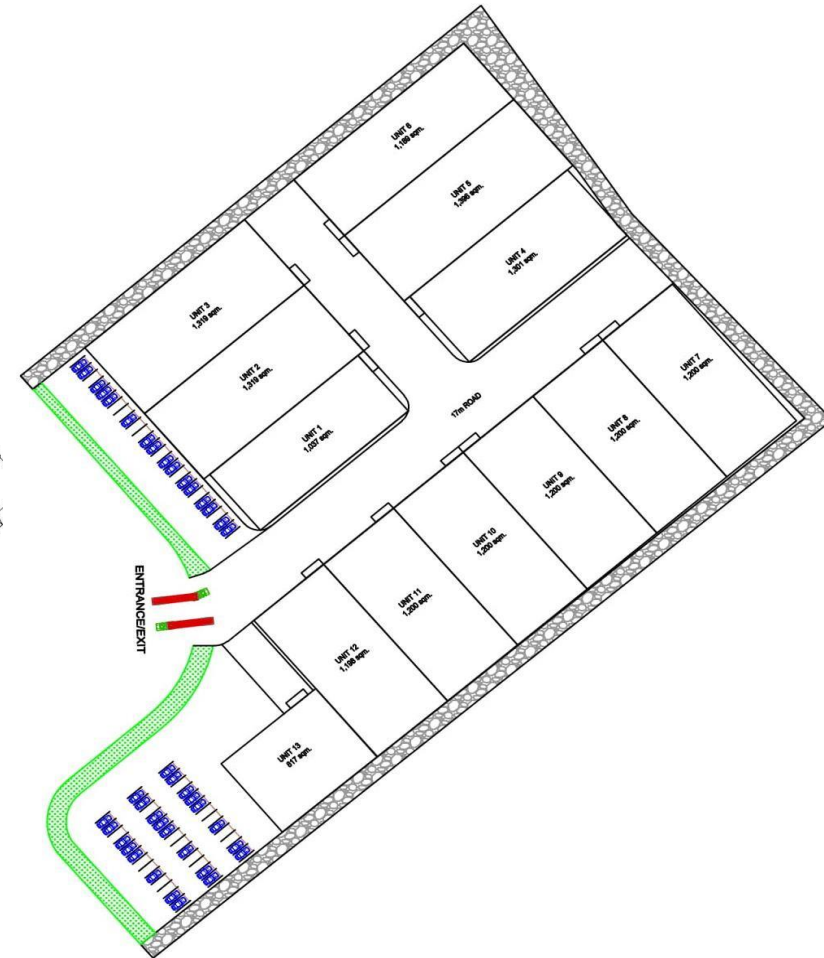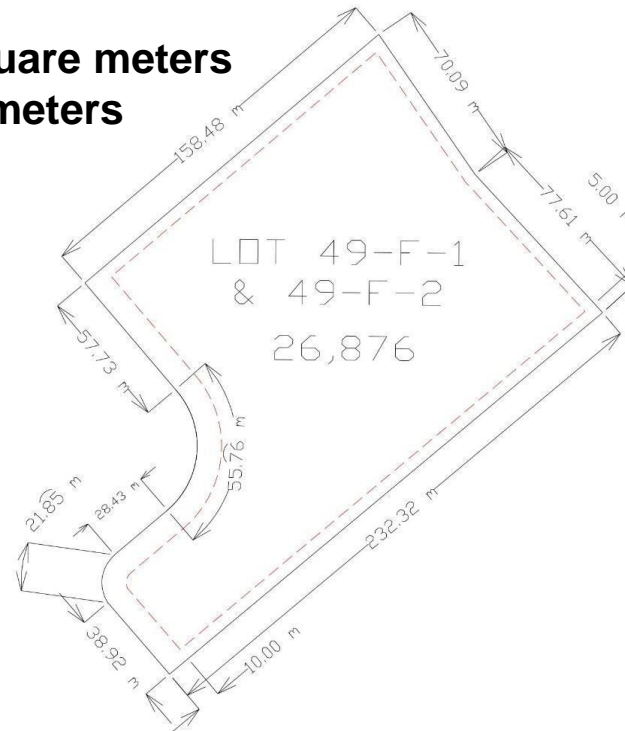

Start of Construction: January 2021  
End of Construction: May 2022

Assessment Date: October 15, 2021  
**Accomplishment To Date: 56.80%**

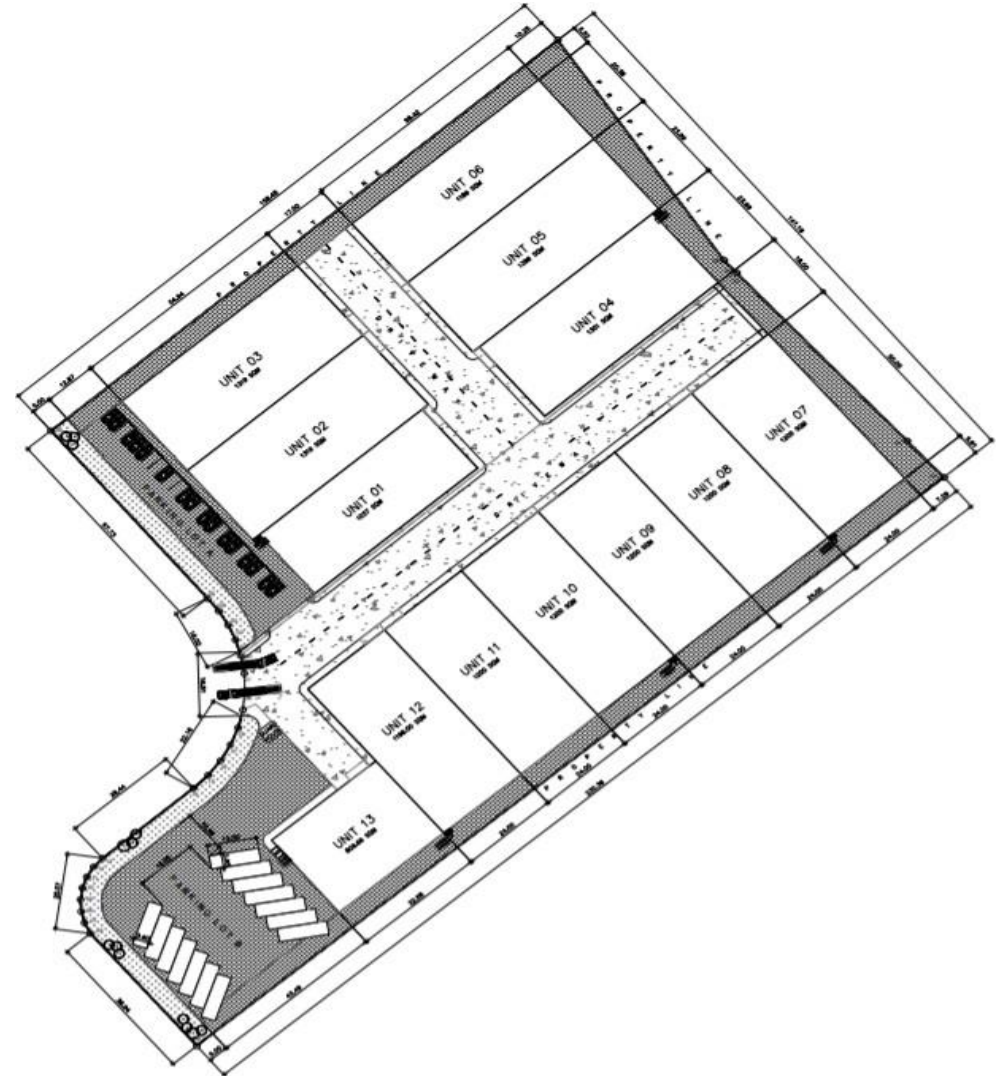

# TURN-OVER SCHEDULE




KEY PLAN

TOTAL LOT AREA = 26,876 sqm.  
TOTAL LEASABLE AREA = 15,576 sqm.

## PHASING SCHEDULE

- PHASE 1 (JANUARY 2021 - DECEMBER 2021)  
TOTAL BUILDING AREA: 4,415 sqm.
- PHASE 2 (MARCH 2021 - MAY 2022)  
TOTAL BUILDING AREA: 4,875 sqm.
- PHASE 3 (MAY 2021 - MAY 2022)  
TOTAL BUILDING AREA: 6,286 sqm.

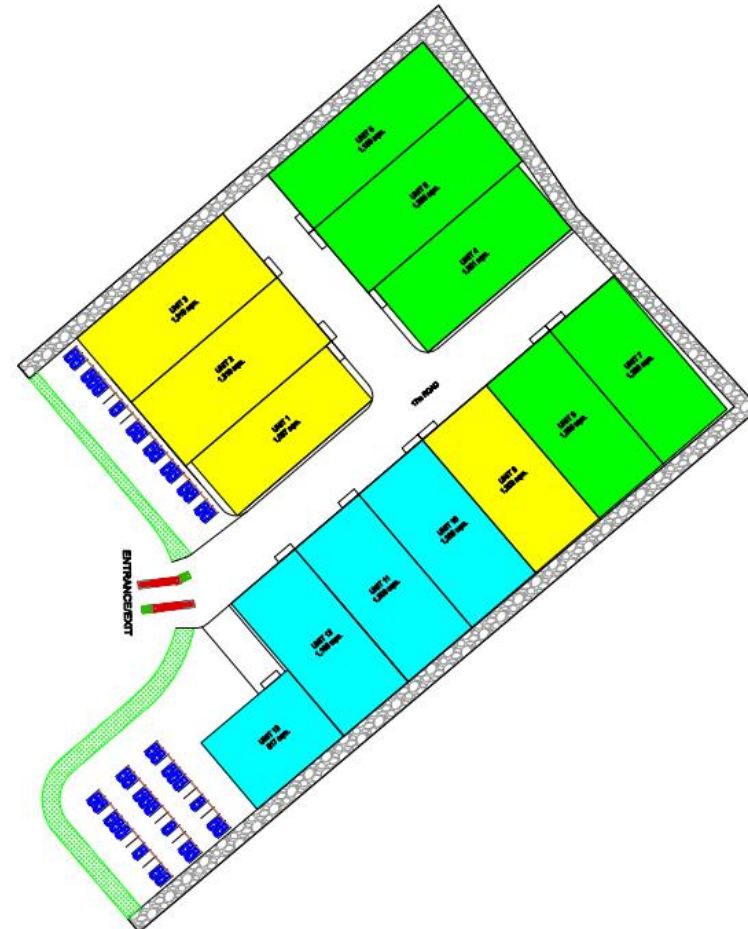

# BUILDING PERSPECTIVE





# BUILDING PERSPECTIVE



## Accomplishment – Masonry, Plastering and Painting at Phase 1






## Accomplishment – Masonry, Plastering and Painting at Phase 1





## Progress Photos at Phase 1

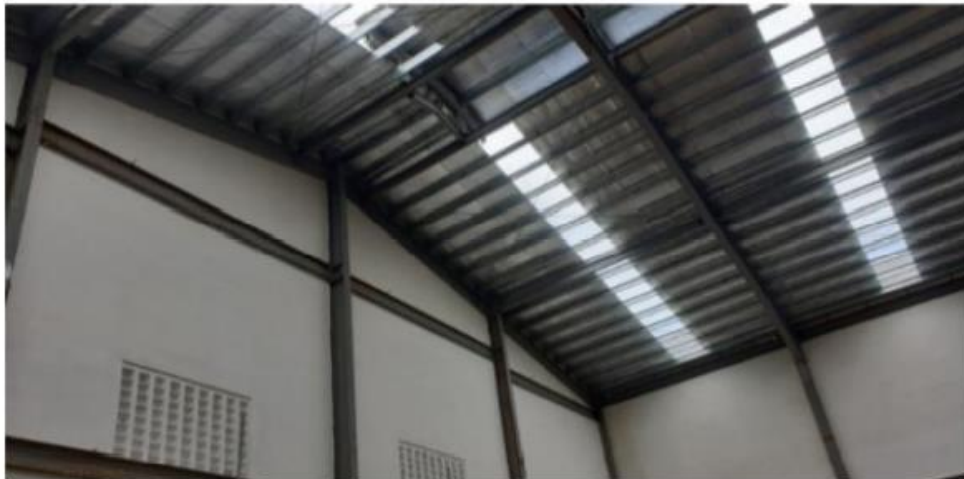

## Accomplishment – Foundation and Tie Beams (Phase 2 and 3)





## Accomplishment – Land Development





---

**END OF UPDATE**
